



# West Park Elementary Project Progress Update #2 January 14<sup>th</sup>, 2020

# **Overall Schedule**

- Design: November 2019 – Summer 2020

- Construction: Summer 2020 - Fall/Winter 2021

# **Overall Budget**

Total Budget	Amount Committed	Spent to Date	Est. Local Expenditures
\$ 34,676,114	\$ 2,375,298	\$ 56,844.81	\$ 719.35

# **Team**

- Owners Rep Dynamic Program Management (DPM)
- Architect Hord Coplan Macht (HCM)
- Construction Contractor FCI Constructors
- Commissioning Agent PCD Engineering
- Environmental Consultant Weecycle Environmental
- Construction Material & 3rd Party Testing Ground Engineering

# **Recently Completed**

- Procurement
  - Environmental Consultant Weecycle Environmental
- Design
  - 12/17/2019 DAG Meeting #4
  - 1/7/2020 DAG Meeting #5
- Budget
  - 12/10/2019 CC-06 #1 submitted for payment

# **In Progress**

- Design
  - Schematic Design thru mid-January (1/16/20)
  - Design Advisory Group (DAG) Meetings
  - User Group Meetings (1/31/20)
  - Coordination with utility providers and local AHJs

# **Upcoming**


# - Procurement

- o Abatement Contractor facilitated by Weecycle
- o FF&E Vendor facilitated by HCM
- Moving Company
- Technology

# Design

- o Continued design progress
- o Contractor estimates of Schematic Design Documents
- Continued coordination with utility providers
- o Permit application submission

# **PHOTOS**

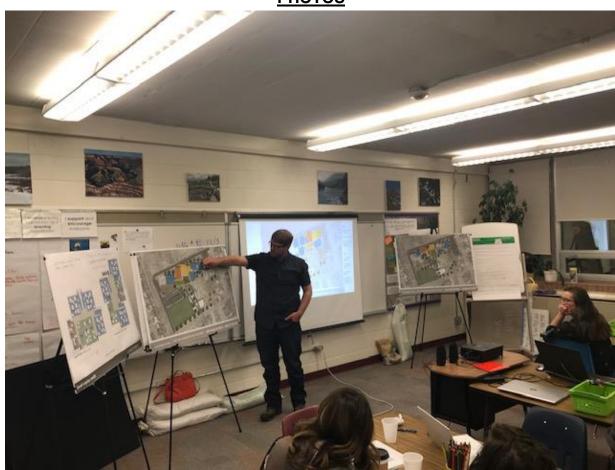

**DAG** #3







DAG #3

# hord coplan macht WEST PARK ELEMENTARY SCHOOL FLOOR PLAN LEGEND ORCOLATION



AAC #4



3/32" = 1'-0"



1800 Warne St., Suite 450 P 303.607.0977 Danner, Celenado 50252 www.fioni2.com

FLOOR PLAN OPTION A

# FLOOR PANILEGEND FLOOR PANILE

**DAG #4** 

FLOOR PLAN OPTION B



3/32" = 1'-0"

