



FCI CONSTRUCTORS, INC.

WEST PARK ELEMENTARY

WEST PARK ELEMENTARY SUPERINTENDENT WEEKLY ACTIVITY REPORT

Report Number 22
Week of 10/24/20 - 10/30/20
Superintendents: Austin Liesmer, Larry Yeager
Author: Larry Yeager



Site Capture #9

CURRENT CONSTRUCTION ACTIVITIES

Enabling Site Work

- Underground Plumbing/Electrical
- Iron Erection @ Area A & B
- Radiant Tubing Install Zone 1,3,4
- Electrical Service Install
- Slab Prep Area A & B
- Light Pole Base Pours
- Basement/ 1st Floor Framing

SITE VISITS

- No Scheduled visits this week


CAPTURED PHOTOS



GYMNASIUM JOISTS



EXTERIOR FRAMING

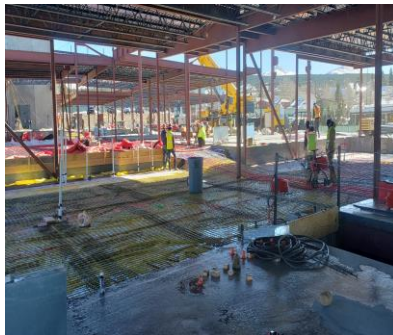

SLAB PREP AREA A



FRAMING @ BASEMENT UPPER LEVEL



MANPOWER COUNT

Trade Partners	Responsibility	Manpower Count
FCI Constructors, Inc.	General Contractor	5, 1 Temp
Schofield	Site Capture/Earthwork/Utilities	0
RMS Concrete	Form/Pour/Finish	10
Reigles	Underground/Radiant Tubing	8
EC Electric	Underground Utility	4
Iron Industries	Iron Erection	12
SWAT	Radon	1
Accurate Insulation	Insulation	2
	Total:	43

WEATHER HISTORY

25	26	27	28	29	30	31
42°	15°	34°	46°	46°	50°	45°
2°	-3°	-9°	6°	20°	15°	19°

- Weather days lost this week: 0
- Weather days to date: 0

FORECASTED WEATHER

1	2	3	4	5	6	7
56° 17°	57° 26°	55° 30°	52° 27°	56° 27°	54° 31°	43° 17°

UPCOMING WEATHER RISK

- No Risks Predicted

SAFETY REPORT

- Lost Time Accidents to Date = 0
- Accidents This Week = 0
- Days without lost time = 174



INSPECTIONS/TESTING REPORT

- All inspection parties present for their responsibilities
 - Rebar Reinforcement (Ground Engineering) - **Ongoing**
 - Concrete Testing (Ground Engineering) - **Ongoing**
 - Electrical Underground (DORA) – **Ongoing**
 - Plumbing Underground (DORA) – **Ongoing**
 - Steel Inspections (Ground Engineering) – **Ongoing**
 - Radiant Heat Pressure Monitoring (Ground Engineering) – **Ongoing**

NEXT WEEK'S ACTIVITIES

- Slab Prep Area A&B
- Area A & B Iron Erection
- Radiant Tubing Install (Slab)
- Roof Decking
- Concrete Slab Pours
- Framing
- Civil Site Work
