



FCI CONSTRUCTORS, INC.

WEST PARK ELEMENTARY

WEST PARK ELEMENTARY

SUPERINTENDENT WEEKLY ACTIVITY REPORT

Report Number 5
Week of 6/20/20 - 6/26/20
Superintendents: Austin Liesmer, Larry Yeager
Author: Jarred Collom



West Park Elementary - Site Capture



CURRENT CONSTRUCTION ACTIVITIES

Enabling Site Work

- Underground Utility Install
- Storm Drain Installation
- Footing form/pour/finish
- Concrete Mobilization
- Electrical Mobilization
- ECE Grading


CONSTRUCTION ACTIVITIES IMAGES



Wall Formwork



Wall Formwork/Rebar
Installation

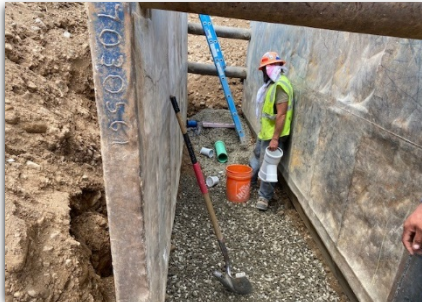

Underground Utility



Underground Utility



New ECE Grading




Wall Formwork



MANPOWER COUNT

Trade Partners	Responsibility	Manpower Count
FCI Constructors, Inc.	General Contractor	4
Schofield	Site Capture/Earthwork/Utilities	9
RMS Concrete	Form/Pour/Finish	10
	Total:	23

WEATHER CONDITIONS



- Weather days this week: 0
- Weather days to date: 0

UPCOMING WEATHER RISKS

- Currently, no weather risks are forecasted.

SAFETY REPORT

- Lost Time Accidents to Date = 0
- Accidents This Week = 0
- Days Without Lost Time = 50

INSPECTIONS/TESTING REPORT

- All inspection parties present for their responsibilities
 - Soil Compaction Testing (Ground Engineering) – **Received 6/10/20**
 - Footing Reinforcement – **Received 6/19/20**
 - Open Hole – **Received 6/15/20**
 - Concrete Test – **Received 6/19/20**

NEXT WEEK'S ACTIVITIES

Site Work

- Underground Utility Install
- Storm Drain Installation
- Form Footings in Gym Area
- Form Walls in Basement Area
- Form Footings Between Gridlines 4A and 9A
