



FCI CONSTRUCTORS, INC.

WEST PARK ELEMENTARY

WEST PARK ELEMENTARY SUPERINTENDENT WEEKLY ACTIVITY REPORT

Report Number 15
Week of 8/29/20 - 9/04/20
Superintendents: Austin Liesmer, Larry Yeager
Author: Larry Yeager



Site
Capture
#2

CURRENT CONSTRUCTION ACTIVITIES

Enabling Site Work

- Underground Plumbing/Electrical @ Basement and Area A/B
- Remaining Pad and Pilaster Forming Area A
- Backfill Lower Walls @ ECE Play Area
- Iron Erection @ Basement Area
- Backfill Basement Wall @ Area A

SITE VISITS

- No site visits were scheduled this week

CAPTURED PHOTOS



BASEMENT SLAB & IRON ERECTION



BACKFILL AREA A @ BASEMENT



SLAB PREP AREA B




LOWER WALLS @ ECE PLAY AREA



MANPOWER COUNT


Trade Partners	Responsibility	Manpower Count
FCI Constructors, Inc.	General Contractor	5
Schofield	Site Capture/Earthwork/Utilities	6
RMS Concrete	Form/Pour/Finish	4
Reigles	Underground Plumbing	5
EC Electric	Underground Utility	3
Accurate Insulation	Waterproofing/Insulation	3
Iron Industries	Steel Erection	5
	Total:	31

WEATHER HISTORY



- Weather days this week: 0
- Weather days to date: 0

FORECASTED WEATHER

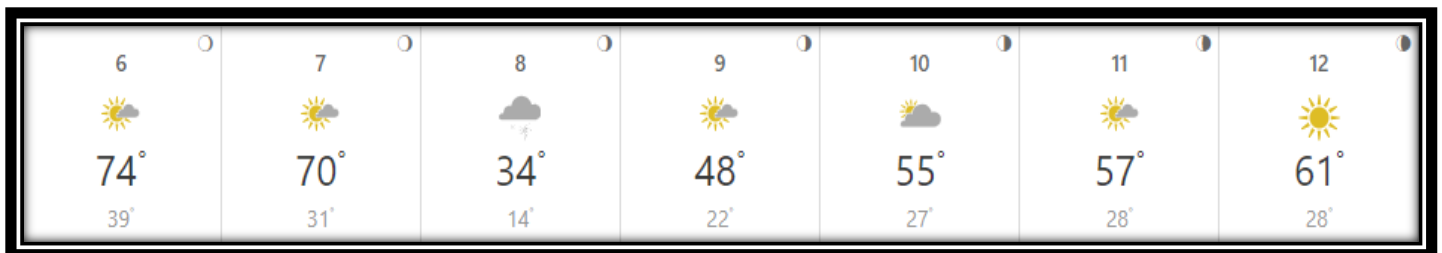

UPCOMING WEATHER RISKS

- Freezing temps which will require winter protection.



SAFETY REPORT

- Lost Time Accidents to Date = **0**
- Accidents This Week = **0**
- Days without lost time = **118**

INSPECTIONS/TESTING REPORT

- All inspection parties present for their responsibilities
 - Soils Testing (Ground Engineering) - **Ongoing**
 - Rebar Reinforcement (Ground Engineering) - **Ongoing**
 - Concrete Testing (Ground Engineering) - **Ongoing**
 - Electrical Underground (DORA) - **Ongoing**
 - Plumbing Underground (DORA) - **Ongoing**
 - Weld Inspections (Ground Engineering) - **Ongoing**

NEXT WEEK'S ACTIVITIES

Site Work

- Plumbing & Electrical Underground Rough - In
- Foundation Backfill/Slab Prep Area B
- Civil Sitework; Upper Lot C&G Prep/Pour, Retaining Wall @ Upper Lot, Paving Prep, South Entrance Curb Cut Prep/Pour
- North Roadway Subgrade Prep
- Area A Iron Erection @ Basement Area
- Pour Remaining Interior Pads & Pilasters Area A
- Radon Mitigation Install Zone 6
- Grease Trap Backfill & Footing Prep/Forming DA, 8A, HB, & Trash Enclosure
