



# FCI CONSTRUCTORS, INC.

WEST PARK ELEMENTARY

## WEST PARK ELEMENTARY SUPERINTENDENT WEEKLY ACTIVITY REPORT

---

Report Number 19  
Week of 9/26/20 - 10/02/20  
*Superintendents: Austin Liesmer, Larry Yeager*  
*Author: Larry Yeager*



**Site Capture #6**



## CURRENT CONSTRUCTION ACTIVITIES

### Enabling Site Work

- Underground Plumbing/Electrical
- Iron Erection @ Area A,B
- Slab Prep Area B Zone 7, Area A Zone 3,4
- Radiant Tubing Install Zone 7
- Upper Lot Paving
- Gas Service Install
- Decking Install @ Basement

### SITE VISITS

- No Onsite Visits Were Made This Week.


### CAPTURED PHOTOS



**PRECAST GYM PANELS & UPPER LOT PAVING**



**UPPER LOT PAVING**

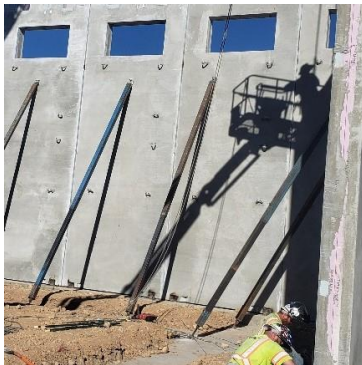

**PRECAST GYM PANEL INSTALL**




**METAL DECKING INSTALL ABOVE BASEMENT**



## MANPOWER COUNT


Trade Partners	Responsibility	Manpower Count
FCI Constructors, Inc.	General Contractor	5, 2 Temps
Schofield	Site Capture/Earthwork/Utilities	6
RMS Concrete	Form/Pour/Finish	5
Reigles	Underground Plumbing	8
EC Electric	Underground Utility	2
Accurate Insulation	Waterproofing/Insulation	0
Iron Industries	Steel Erection	7
Stresscon	Precast Gym Panels	9
	<b>Total:</b>	<b>44</b>

## WEATHER HISTORY



- **Weather days lost this week: 0**
- **Weather days to date: 0**

## FORECASTED WEATHER



## UPCOMING WEATHER RISK

- **No weather risks predicted**

## SAFETY REPORT

- Lost Time Accidents to Date = 0
- Accidents This Week = 0
- Days without lost time = **146**



## **INSPECTIONS/TESTING REPORT**

- All inspection parties present for their responsibilities
  - Soils Testing (Ground Engineering) - **Ongoing**
  - Rebar Reinforcement (Ground Engineering) - **Ongoing**
  - Concrete Testing (Ground Engineering) - **Ongoing**
  - Electrical Underground (DORA) – **Ongoing**
  - Plumbing Underground (DORA) – **Ongoing**
  - Steel Inspections (Ground Engineering) – **Ongoing**
  - Radiant Heat Pressure Monitoring (Ground Engineering) – **Ongoing**
  - Paving Inspections (Ground Engineering) - **Ongoing**

## **NEXT WEEK'S ACTIVITIES**

- Plumbing & Electrical Underground
- Slab Prep Area B (Zone 4)
- ECE Play Area Retaining Wall,
- Area A & B Iron Erection
- Radiant Tubing Install (Zone 7)
- Slab Pour Zone 7
- Precast Panel Erection
- Paving Roadway
- Curb & Gutter on Harrison Ave
- Electrical Service Install
- Slab On Deck Prep
- Radon mitigation install (Zone 4)
