



FCI CONSTRUCTORS, INC.

WEST PARK ELEMENTARY

WEST PARK ELEMENTARY SUPERINTENDENT WEEKLY ACTIVITY REPORT

Report Number 30
Weeks of 1/2/21 – 1/9/21
Superintendents: Austin Liesmer, Larry Yeager
Author: Larry Yeager



Site Capture #17

CURRENT CONSTRUCTION ACTIVITIES

Enabling Site Work

- Area A & B Exterior/Interior Framing
- Exterior Sheathing
- MEP Rough-in
- Upper Drywall/Drywall Stock
- Roofing @ Area A/B
- Diamond Pour Back
- In Wall Backing
- Canopy Framing
- Floor Grinding (Slurry Coat)
- Drywall Stock

SITE VISITS

- Flashing Detail Coordination Meeting
- Ben Graham with PCD Engineering


CAPTURED PHOTOS



GYMNASIUM ROUND DUCT INSTALL



(SLURRY COAT) FILLER/FLOOR PROTECTANT

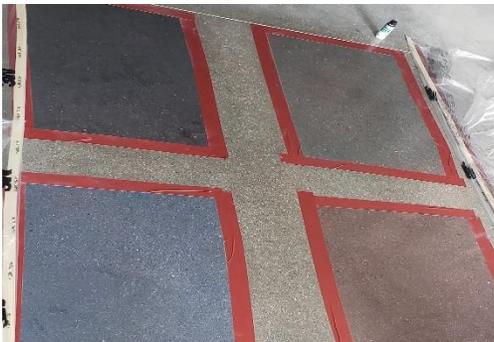

POLISHED FLOOR & SAMPLE COLORS



CRAWLSPACE



MANPOWER COUNT


Trade Partners	Responsibility	Manpower Count
FCI Constructors, Inc.	General Contractor	6 FCI, & 7 Temps
Schofield	Site Capture/Earthwork/Utilities	0
RMS Concrete	Site Concrete	11
Reigles	Plumbing & Mechanical	13
EC Electric	Electrical	11
Iron Industries	Iron Erection/Roof Decking	2
Service West	Framing	20
Skyline Contractors	Roofing	9
Concrete Visions	Floor Polishing	6
Stresscon	Precast Panels	3
	TOTAL:	88

WEATHER HISTORY



- Weather days lost this week: 0
- Weather days to date: 0

FORECASTED WEATHER

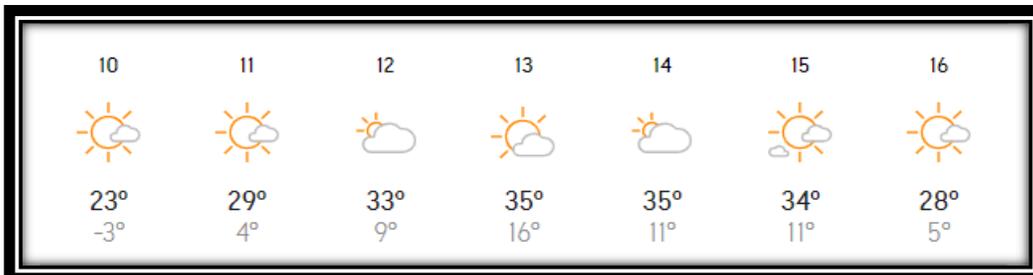

UPCOMING WEATHER FORECAST

- Clear Days, Cold Nighttime Temps



SAFETY REPORT

- Lost Time Accidents to Date = **0**
- Accidents This Week = **0**
- Days without lost time = **244**

INSPECTIONS/TESTING REPORT

- All inspection parties present for their responsibilities
 - Concrete Reinforcement (Ground Engineering) - **Ongoing**
 - Concrete/Asphalt Testing (Ground Engineering) – **Ongoing**
 - Mechanical (Ground Engineering) - **Ongoing**
 - Electrical (DORA) – **Ongoing**
 - Plumbing (DORA) – **Ongoing**
 - In Floor Heat/Snow Melt (Ground Engineering) - **Ongoing**
 - Steel Inspections (Ground Engineering) – **Ongoing**
 - Roofing (Ground Engineering) – **Ongoing**
 - Framing Inspections (Ground Engineering) – **Ongoing**
 - Envelope Tightness (PCD Engineering) – **Ongoing**

NEXT WEEK'S ACTIVITIES

- Roofing
- MEP Rough-in
- Interior Framing Area A/B
- Interior Drywall Area A
- Upper Drywall Area B
- Glu-Lam Canopy Framing
- Canopy Roof Decking
- Acoustic Insulation
- Interior Pre-Cast Patching @ Gymnasium
- Slurry Coat on Polished Floors



FCI CONSTRUCTORS, INC.
WEST PARK ELEMENTARY

SUPERINTENDENT'S WEEKLY ACTIVITY REPORT

NUMBER 30 | Weeks of 1/2/21 – 1/9/21

West Park Elementary

Austin Liesmer, Larry Yeager
