



FCI CONSTRUCTORS, INC.

WEST PARK ELEMENTARY

WEST PARK ELEMENTARY SUPERINTENDENT WEEKLY ACTIVITY REPORT

Report Number 36
Weeks of 2/13/21 – 2/19/21
Superintendents: Austin Liesmer, Larry Yeager
Author: Larry Yeager



SITE CAPTURE #23

CURRENT CONSTRUCTION ACTIVITIES


Enabling Site Work

- Interior Framing
- MEP Rough-in
- Roofing @ Area A/B
- In Wall Backing
- Fire Suppression Rough-in
- Tape and Finish Drywall Area A (Window Returns)
- Acoustic Insulation
- Brick Veneer
- Window Frame/Glazing Install
- Prime and Paint
- Low Volt Rough-in

SITE VISITS

- Leadville Fireman Crew - School Tour

CAPTURED PHOTOS

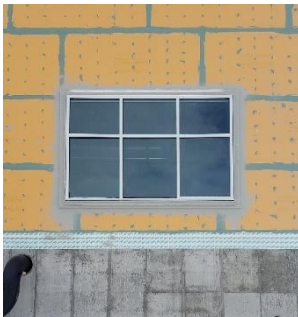

GLAZING INSTALL



GLAZING INSTALL



BRICK ACCENT BANDS



BRICK/PRECAST INSTALL



MANPOWER COUNT


Trade Partners	Responsibility	Manpower Count
FCI Constructors, Inc.	General Contractor	9 FCI, & 1 Temp
Schofield	Site Capture/Earthwork/Utilities	0
RMS Concrete	Site Concrete	0
Reigles	Plumbing & Mechanical	19
EC Electric	Electrical	15
Iron Industries	Iron Erection/Roof Decking	0
Service West	Framing	10
Skyline Contractors	Roofing	0
Concrete Visions	Floor Polishing	0
Stresscon	Precast Panels	3
Swat Group	Radon	0
Excel Fire Protection	Fire Suppression	4
ASCO Construction, LLC	Brick Veneer/Masonry	10
Summit Sealants	Sealants/Caulking	0
Innovative Painting	Painting	6
Eagle Valley Glass	Glazing	5
	TOTAL:	82

WEATHER HISTORY



- Weather days lost this week: 0
- Weather days to date: 0

FORECASTED WEATHER



UPCOMING WEATHER FORECAST

- Overnight lows in the single digits. No snow predicted during the week.

SAFETY REPORT

- Lost Time Accidents to Date = **0**
- Accidents This Week = **0**
- Days without lost time = **286**

INSPECTIONS/TESTING REPORT

- All inspection parties present for their responsibilities.
 - Concrete Reinforcement (Ground Engineering) - **Ongoing**
 - Concrete/Asphalt Testing (Ground Engineering) – **Ongoing**
 - Mechanical (Ground Engineering) - **Ongoing**
 - Electrical (DORA) – **Ongoing**
 - Plumbing (DORA) – **Ongoing**
 - In Floor Heat/Snow Melt (Ground Engineering) - **Ongoing**
 - Steel Inspections (Ground Engineering) – **Ongoing**
 - Roofing (Ground Engineering) – **Ongoing**
 - Framing Inspections (Ground Engineering) – **Ongoing**
 - Envelope Tightness (PCD Engineering) – **Ongoing**
 - Exterior Insulation (Ground Engineering) – **Ongoing**
 - Duct Inspection (Ground Engineering) - **Ongoing**

NEXT WEEK'S ACTIVITIES

- MEP Rough-in
- Low Volt Rough-in
- Seal Wall Penetrations
- Interior Framing Area A/B
- Hang/Tape/Finish Drywall Area A/B
- Frame Hard Lids & Soffits
- Hard Lid Rough-in
- Fire Suppression Rough-in
- Acoustic Insulation Area B
- Set Window Frames/Glazing
- Finish Window Returns
- Exterior Insulation/Brick Veneer
- Form/Pour Housekeeping Pads
- Paint
