




# FCI CONSTRUCTORS, INC.

WEST PARK ELEMENTARY

## WEST PARK ELEMENTARY SUPERINTENDENT WEEKLY ACTIVITY REPORT

---

Report Number 49  
Weeks of 5/22/21 – 5/28/21  
*Superintendents: Austin Liesmer, Larry Yeager*  
*Author: Larry Yeager*

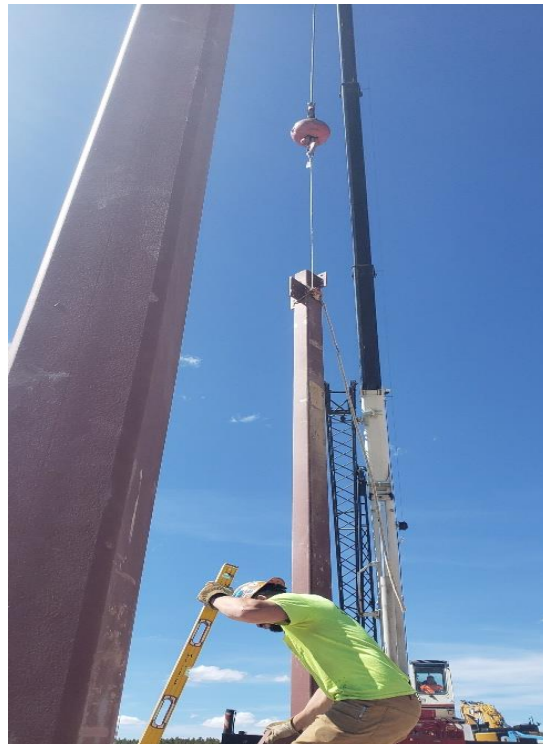

**SITE CAPTURE #36**

## **CURRENT CONSTRUCTION ACTIVITIES**

### **Enabling Site Work**

- MEP Rough-in/Trim
- Site Sub-grade Prep/Pour
- Fire Suppression Trim
- Tape and Finish Drywall Area B/Commons
- Pipe/Duct Insulation
- Brick Veneer
- Ceiling Tile Drop
- Interior Prime and Paint
- Wall Tile/Carpet Install
- Low Volt Rough-in
- Classroom Grid Ceiling Install
- Exterior Snowmelt Main Line Install
- Specialties install Div. 10

### **SITE VISITS**

- No Visits Scheduled

### **CAPTURED PHOTOS**



**SIDEWALK @ 12<sup>TH</sup> ENTRANCE**



**FIREPLACE MANTLE**



**FIRE RISER ENTRY**




**ADDITION IRON ERECTION**




## MANPOWER COUNT

| Trade Partners                | Responsibility                | Manpower Count |
|-------------------------------|-------------------------------|----------------|
| FCI Constructors, Inc.        | General Contractor            | 6 FCI, 1Temp   |
| Schofield                     | Excavation                    | 7              |
| Reigles/Airtech               | Plumbing & Mechanical         | 22             |
| EC Electric/Sterling/Linx     | Electrical                    | 22             |
| Service West                  | Framing/Drywall/Grid Ceilings | 5              |
| Colorado Floorworks           | Tile/Carpet                   | 1              |
| Concrete Visions              | Floor Polishing               | 4              |
| Iron Industries               | Iron Erection                 | 5              |
| Excel Fire Protection         | Fire Suppression              | 1              |
| ASCO Construction, LLC        | Brick Veneer/Masonry          | 15             |
| Specialties Contracting, Inc. | Specialties                   | 3              |
| Innovative Painting           | Painting                      | 3              |
| RMS                           | Concrete                      | 4              |
| Sidney Millworks              | Casework                      | 0              |
| Eagle Valley Glass and Mirror | Glazing                       | 4              |
| Arapahoe Sign Arts            | Signage                       | 2              |
| Omni Tech Industries          | Resinous Flooring             | 5              |
| <b>Total:</b>                 |                               | <b>110</b>     |

## WEATHER HISTORY



## FORECASTED WEATHER



## UPCOMING WEATHER FORECAST

- **High temps reaching the 60's by the end of the week. Overnight lows above FREEZING!**



## **SAFETY REPORT**

- Lost Time Accidents to Date = **0**
- Accidents This Week = **0**
- Days without lost time = **391**

## **INSPECTIONS/TESTING REPORT**

- **All inspection parties present for their responsibilities.**
- Concrete/Reinforcement (Ground Engineering) - **Ongoing**
- Concrete/Asphalt Testing (Ground Engineering) – **Ongoing**
- Mechanical (Ground Engineering) - **Ongoing**
- Electrical (DORA) – **Ongoing**
- Plumbing (DORA) – **Ongoing**
- In Floor Heat/Snow Melt (Ground Engineering) - **Ongoing**
- Steel Inspections (Ground Engineering) – **Ongoing**
- Roofing (Ground Engineering) – **Ongoing**
- Framing Inspections (Ground Engineering) – **Ongoing**
- Envelope Tightness (PCD Engineering) – **Ongoing**
- Exterior Insulation (Ground Engineering) – **Ongoing**
- Duct Inspection (Ground Engineering) – **Ongoing**
- Fire Suppression (Leadville Fire) - **Ongoing**

## **NEXT WEEK'S ACTIVITIES**

- MEP Rough-in/Trim
- Addition Roof Decking
- Low Volt Rough-in
- Hang/Tape/Finish Drywall Area B/Commons
- Fire Suppression Trim
- LVT/Carpet Install
- Resinous Flooring
- Bathroom Accessories
- Water Entry
- Ceiling Tile Drop
- Exterior Insulation/Brick Veneer
- Interior Prime and Paint
- Grid Ceiling Install
- Civil Site Prep/Pour
- MEP Trim
