



FCI CONSTRUCTORS, INC.
WEST PARK ELEMENTARY

WEST PARK ELEMENTARY
SUPERINTENDENT WEEKLY ACTIVITY REPORT

Report Number 53
Weeks of 7/10/21 – 7/16/21
Superintendents: Austin Liesmer, Larry Yeager
Author: Larry Yeager



SITE CAPTURE #41



CURRENT CONSTRUCTION ACTIVITIES

Enabling Site Work

- MEP Rough-in/Trim
- Site Sub-grade Prep/Topsoil Placement
- Site Concrete Placement
- Fire Suppression Trim
- Interior/Exterior Railing Install
- Trade Deficiencies
- Kitchen Equipment Install
- Interior/Exterior Window, Veneer Control Joint Sealing
- Ceiling Tile Drop
- Interior/Exterior Prime and Paint
- Low Volt Trim Out
- Exterior Snowmelt Install
- School Furniture
- Final Cleaning

SITE VISITS

- David Chadwell, Steve Boyle

CAPTURED PHOTOS



CLASSROOM FURNITURE



WALL GRAPHICS



BIG #@\$@ FAN

UTILITY YARD



MANPOWER COUNT


Trade Partners	Responsibility	Manpower Count
FCI Constructors, Inc.	General Contractor	8 & 4 Temps
Schofield	Excavation	8
Reigles	Plumbing & Mechanical	22
EC Electric	Electrical	16
Service West	Framing/Drywall/Grid Ceilings	8
Colorado Floorworks	Tile/Carpet	4
RMS	Site Concrete	8
Iron Industries	Iron Erection	4
Excel Fire Protection	Fire Suppression	1
Fountaine Design Group dba FDG Products	Metal Panels	5
Innovative Painting	Painting	5
Sidney Millworks	Casework	2
Eagle Valley Glass and Mirror	Glazing	4
Grady's Restaurant and Bar Supply	Kitchen Equipment	0
Total:		99

WEATHER HISTORY



- Weather days lost this week: 0
- Weather days to date: 0

FORECASTED WEATHER

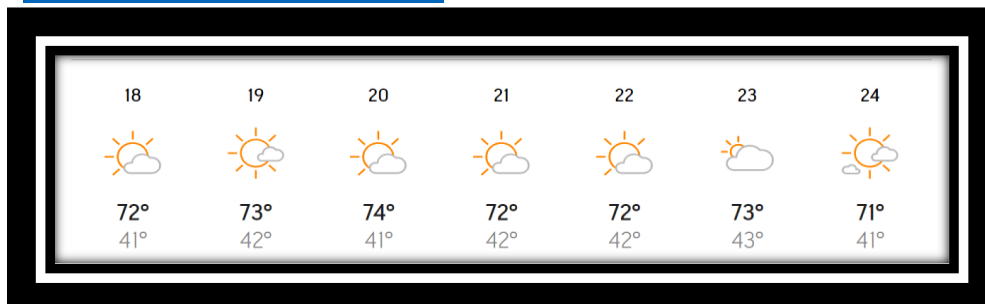

UPCOMING WEATHER FORECAST

- Very pleasant forecasted week ahead .



SAFETY REPORT

- Lost Time Accidents to Date = **0**
- Accidents This Week = **0**
- Days without lost time = **433**

INSPECTIONS/TESTING REPORT

- **All inspection parties present for their responsibilities.**
- Concrete Reinforcement (Ground Engineering) - **Ongoing**
- Concrete/Asphalt Testing (Ground Engineering) – **Ongoing**
- Mechanical (Ground Engineering) - **Ongoing**
- Electrical (DORA) – **Ongoing**
- Plumbing (DORA) – **Ongoing**
- In Floor Heat/Snow Melt (Ground Engineering) - **Ongoing**
- Steel Inspections (Ground Engineering) – **Ongoing**
- Roofing (Ground Engineering) – **Ongoing**
- Framing Inspections (Ground Engineering) – **Ongoing**
- Envelope Tightness (PCD Engineering) – **Ongoing**
- Exterior Insulation (Ground Engineering) – **Ongoing**
- Duct Inspection (Ground Engineering) – **Ongoing**
- Fire Suppression (Leadville Fire) - **Ongoing**

NEXT WEEK'S ACTIVITIES

- MEP Rough-in/Trim
- MEP Start-up
- Low Volt Tim Out
- Addition Interior/Exterior Framing/Sheathing
- Specialties Install
- Ceiling Tile Drop
- Interior/Exterior Prime and Paint
- Grid Ceiling Install
- Civil Site Topsoil/Prep/Pour
- MEP Trim Out
- School Furniture
- Deficiency Walk
- Kitchen Equipment Install
- Final Cleaning
- Abatement
